

ID	Task Mod	Task Name	Duration	Start	Finish	Predecessors	Resource Names	January 2019														February 2019					
								16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	2	5	8	11
1	🚀	PHASE I (EXPLORATORY WORK)	10 days	Mon 9/17/18	Fri 9/28/18		CONTRACTOR																				
2	📄	TRAFFIC CONTROL PLAN	3 days	Mon 9/17/18	Wed 9/19/18		OFFICE																				
3	📄	MOBILIZATION	2 days	Thu 9/20/18	Fri 9/21/18	2	PP/CC																				
4	📄	EROSION CONTROL	3 days	Tue 9/18/18	Thu 9/20/18		CORPAC																				
5	📄	TEMPORARY SIGNING	3 days	Wed 9/19/18	Fri 9/21/18		EGAMI																				
6	📄	MAINLINE SEWER TV & CLEAN	3 days	Thu 9/20/18	Mon 9/24/18		PROPIPE																				
7	📄	LATERAL SEWER LINE TV & CLEAN	3 days	Mon 9/24/18	Wed 9/26/18		PROPIPE																				
8	📄	POTHOLE (ID EXISTING UTILITIES)	3 days	Wed 9/26/18	Fri 9/28/18		PROPIPE																				
9	🚀	SAVIER ST SEWER	26 days	Mon 12/17/18	Fri 1/25/19																						
10	📄	SUBMIT AZIMUTH SUBCONTRACT FOR APPROVAL	28 days	Fri 12/14/18	Mon 1/28/19		PBOT																				
11	📄	24" SEWER PIPE 100' MH #12 TO MH #13	6 days	Mon 2/4/19	Mon 2/11/19		ASIMUTH																				
12	📄	24" SEWER PIPE 335' MH #13 TO MH #14	10 days	Tue 2/12/19	Mon 2/25/19	11	ASIMUTH																				
13	📄	ASPHALT DITCH PAVING	2 days	Tue 2/26/19	Wed 2/27/19	12	CORPAC																				
14	🚀	THURMAN - (20+65 TO 28+51) & PATH - (TO 151+00)	51 days	Wed 1/2/19	Wed 3/13/19																						
15	📄	EXCAVATION	25 days	Fri 1/25/19	Thu 2/28/19		CORPAC																				
16	📄	AGG BASE	28 days	Mon 1/28/19	Wed 3/6/19		CORPAC																				
17	📄	ELECTRICAL	12 days	Mon 2/4/19	Tue 2/19/19	31	GLOBAL																				
18	📄	NW THURMAN ST. SEWER	14 days	Mon 2/25/19	Thu 3/14/19																						
19	📄	12" SEWER 263' MH #49, #23, #48, & #24	6 days	Mon 2/25/19	Mon 3/4/19		ASIMUTH																				
20	📄	STORM DRAIN	8 days	Tue 3/5/19	Thu 3/14/19	19	ASIMUTH																				
21	📄	CURB AND SIDEWALK PREP	10 days	Mon 2/18/19	Fri 3/1/19		CORPAC																				
22	📄	POUR CURB & SIDEWALKS	10 days	Thu 2/21/19	Wed 3/6/19		R&R																				
23	📄	PAVE BASE LIFT (WEATHER DEPENDANT)	2 days	Mon 3/11/19	Tue 3/12/19		KODIAK																				
24	📄	20TH AVE - SAVIER TO THURMAN (3+60 TO 5+50)	17 days	Mon 3/4/19	Tue 3/26/19																						
25	📄	EXCAVATION	13 days	Mon 3/4/19	Wed 3/20/19		CORPAC																				
26	📄	STORMWATER PLANTERS	2 days	Tue 3/5/19	Wed 3/6/19		CORPAC																				
27	📄	CURB AND SIDEWALK PREP	5 days	Mon 3/18/19	Fri 3/22/19		CORPAC																				
28	📄	AGG BASE	15 days	Mon 3/4/19	Fri 3/22/19		CORPAC																				
29	📄	BASE PAVE	2 days	Mon 3/25/19	Tue 3/26/19																						
30	📄	20TH (SAVIER TO THURMAN) SUBS	18 days	Thu 3/7/19	Mon 4/1/19																						
31	📄	ELECTRICAL	5 days	Thu 3/7/19	Wed 3/13/19		GLOBAL																				
32	📄	POUR CURB & SIDEWALKS	6 days	Wed 3/20/19	Wed 3/27/19		R&R																				
33	📄	PAVE BASE LIFT (WEATHER DEPENDANT)	1 day	Mon 4/1/19	Mon 4/1/19		KODIAK																				
34	📄	PATH - 151+00 TO 19TH AVE	14 days	Tue 4/2/19	Fri 4/19/19																						
35	📄	REMOVAL OF STRUCTURES AND OBSTRUCTIONS	5 days	Tue 4/2/19	Mon 4/8/19	33	CORPAC																				

Project: 20TH AVE. LID
Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mod	Task Name	Duration	Start	Finish	Pred	Resource Names	January 2019							February 2019																						
								16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30	2	5	8	11										
36	🚧	EXCAVATION	8 days	Tue 4/9/19	Thu 4/18/19	35	CORPAC																														
37	🚧	AGG BASE	8 days	Wed 4/10/19	Fri 4/19/19		CORPAC																														
38	🚧	CURB AND SIDEWALK PREP	4 days	Mon 4/15/19	Thu 4/18/19		CORPAC																														
39	🚧	POUR CURB & SIDEWALKS	3 days	Wed 4/17/19	Fri 4/19/19	38	R&R																														
40	🚧	20TH AVE - SAVIER TO RALEIGH (0+32 TO 3+60)	21 days	Mon 3/25/19	Mon 4/22/19																																
41	🚧	EXCAVATION	15 days	Mon 3/25/19	Fri 4/12/19	28	CORPAC																														
42	🚧	ELECTRICAL	5 days	Thu 3/28/19	Wed 4/3/19		GLOBAL																														
43	🚧	AGG BASE	15 days	Tue 3/26/19	Mon 4/15/19		CORPAC																														
44	🚧	STORMWATER PLANTERS	2 days	Mon 4/1/19	Tue 4/2/19		CORPAC																														
45	🚧	CURB AND SIDEWALK PREP	5 days	Mon 4/1/19	Fri 4/5/19		CORPAC																														
46	🚧	POUR CURB & SIDEWALKS	6 days	Wed 4/10/19	Wed 4/17/19		R&R																														
47	🚧	PAVE BASE LIFT (WEATHER DEPENDANT)	1 day	Mon 4/22/19	Mon 4/22/19	46	KODIAK																														
48	🚧	20TH (SAVIER TO RALEIGH) SEWER	13 days	Fri 3/15/19	Tue 4/2/19																																
49	🚧	15" SEWER PIPE 186' MH #14 TO MH #52	4 days	Fri 3/15/19	Wed 3/20/19	20	ASIMUTH																														
50	🚧	15" SEWER 23' MH #52 TO MH #51	2 days	Thu 3/21/19	Fri 3/22/19	49	ASIMUTH																														
51	🚧	15" SEWER 57' MH #51 TO MH #19	2 days	Mon 3/25/19	Tue 3/26/19	50	ASIMUTH																														
52	🚧	STORM DRAIN	5 days	Wed 3/27/19	Tue 4/2/19	51	ASIMUTH																														
53	🚧	23RD ST. INTERCHANGE	50 days	Mon 3/18/19	Fri 5/24/19																																
54	🚧	REMOVAL OF ST & OBST	3 days	Mon 3/18/19	Wed 3/20/19		CORPAC																														
55	🚧	ELECTRICAL IN GROUND WORK	10 days	Tue 3/19/19	Mon 4/1/19		GLOBAL																														
56	🚧	STORM DRAIN	4 days	Thu 3/28/19	Tue 4/2/19	52	ASIMUTH																														
57	🚧	PREP FOR CURBS, SIDEWALK & ISLANDS	10 days	Thu 4/4/19	Wed 4/17/19	56	CORPAC																														
58	🚧	POUR CURB & SIDEWALKS & ISLANDS	15 days	Mon 4/8/19	Fri 4/26/19		R&R																														
59	🚧	ELECTRICAL - ABOVE GROUND	25 days	Mon 3/25/19	Fri 4/26/19		GLOBAL																														
60	🚧	PAVEMENT REPAIRS	3 days	Mon 4/29/19	Wed 5/1/19	58	CORPAC																														
61	🚧	PAVE (WEATHER DEPENDANT)	3 days	Wed 5/1/19	Fri 5/3/19																																
62	🚧	19TH AVE. INTERCHANGE	22 days	Mon 4/8/19	Tue 5/7/19																																
63	🚧	REMOVAL OF ST & OBST	3 days	Mon 4/8/19	Wed 4/10/19		CORPAC																														
64	🚧	ELECTRICAL IN GROUND WORK	5 days	Tue 4/9/19	Mon 4/15/19		GLOBAL																														
65	🚧	STORM DRAIN	4 days	Wed 4/3/19	Mon 4/8/19	56	ASIMUTH																														
66	🚧	PREP FOR CURBS, SIDEWALK & ISLANDS	10 days	Thu 4/11/19	Wed 4/24/19		CORPAC																														
67	🚧	POUR CURB & SIDEWALKS & ISLANDS	12 days	Mon 4/15/19	Tue 4/30/19		R&R																														
68	🚧	ELECTRICAL - ABOVE GROUND	10 days	Thu 4/11/19	Wed 4/24/19		GLOBAL																														
69	🚧	PAVEMENT REPAIRS	3 days	Mon 4/29/19	Wed 5/1/19		CORPAC																														
70	🚧	PAVE	3 days	Wed 5/1/19	Fri 5/3/19		CORPAC																														



Project: 20TH AVE. LID
Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

ID	Task Mod	Task Name	Duration	Start	Finish	Prede	Resource Names	January 2019							February 2019								
								16	19	22	25	28	31	3	6	9	12	15	18	21	24	27	30
71	➤	20TH AVE - THURMAN TO UPSHUR (5+50 TO 9+00)	35 days	Mon 5/13/19	Fri 6/28/19																		
72	⚑	REMOVAL OF STRUCTURES AND OBSTRUCTIONS	5 days	Mon 5/13/19	Fri 5/17/19		CORPAC																
73	⚑	EXCAVATION	14 days	Wed 5/15/19	Mon 6/3/19		CORPAC																
74	➤	ELECTRICAL	4 days	Mon 5/20/19	Thu 5/23/19		GLOBAL																
75	⚑	AGG BASE	10 days	Fri 5/17/19	Thu 5/30/19		CORPAC																
76	⚑	STORMWATER PLANTERS	5 days	Thu 5/30/19	Wed 6/5/19		CORPAC																
77	⚑	CURB AND SIDEWALK PREP	5 days	Thu 5/30/19	Wed 6/5/19		CORPAC																
78	➤	POUR CURB & SIDEWALKS	6 days	Mon 6/3/19	Mon 6/10/19		R&R																
79	➤	PAVE BASE LIFT	1 day	Thu 6/13/19	Thu 6/13/19		KODIAK																
80	➤	UPSHUR	25 days	Mon 4/29/19	Fri 5/31/19																		
81	⚑	REMOVAL OF STRUCTURES AND OBSTRUCTIONS	5 days	Tue 4/30/19	Mon 5/6/19		CORPAC																
82	⚑	EXCAVATION	14 days	Thu 5/2/19	Tue 5/21/19		CORPAC																
83	⚑	AGG BASE	21 days	Fri 5/3/19	Fri 5/31/19		CORPAC																
84	➤	ELECTRICAL	4 days	Mon 5/6/19	Thu 5/9/19		GLOBAL																
85	⚑	CURB AND SIDEWALK PREP	5 days	Mon 5/13/19	Fri 5/17/19		CORPAC																
86	➤	POUR CURB & SIDEWALKS	6 days	Thu 5/16/19	Thu 5/23/19		R&R																
87	➤	PAVE BASE LIFT	1 day	Mon 5/27/19	Mon 5/27/19		KODIAK																
88	➤	PERMANENT SIGNING	5 days	Mon 6/3/19	Fri 6/7/19		EGAMI																
89	➤	LANDSCAPING	5 days	Mon 6/3/19	Fri 6/7/19																		
90	➤	TOP LIFT PAVING	5 days	Mon 6/17/19	Fri 6/21/19		KODIAK																
91	➤	STRIPING	3 days	Fri 6/28/19	Tue 7/2/19		APPLY A LINE																


Project: 20TH AVE. LID
Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

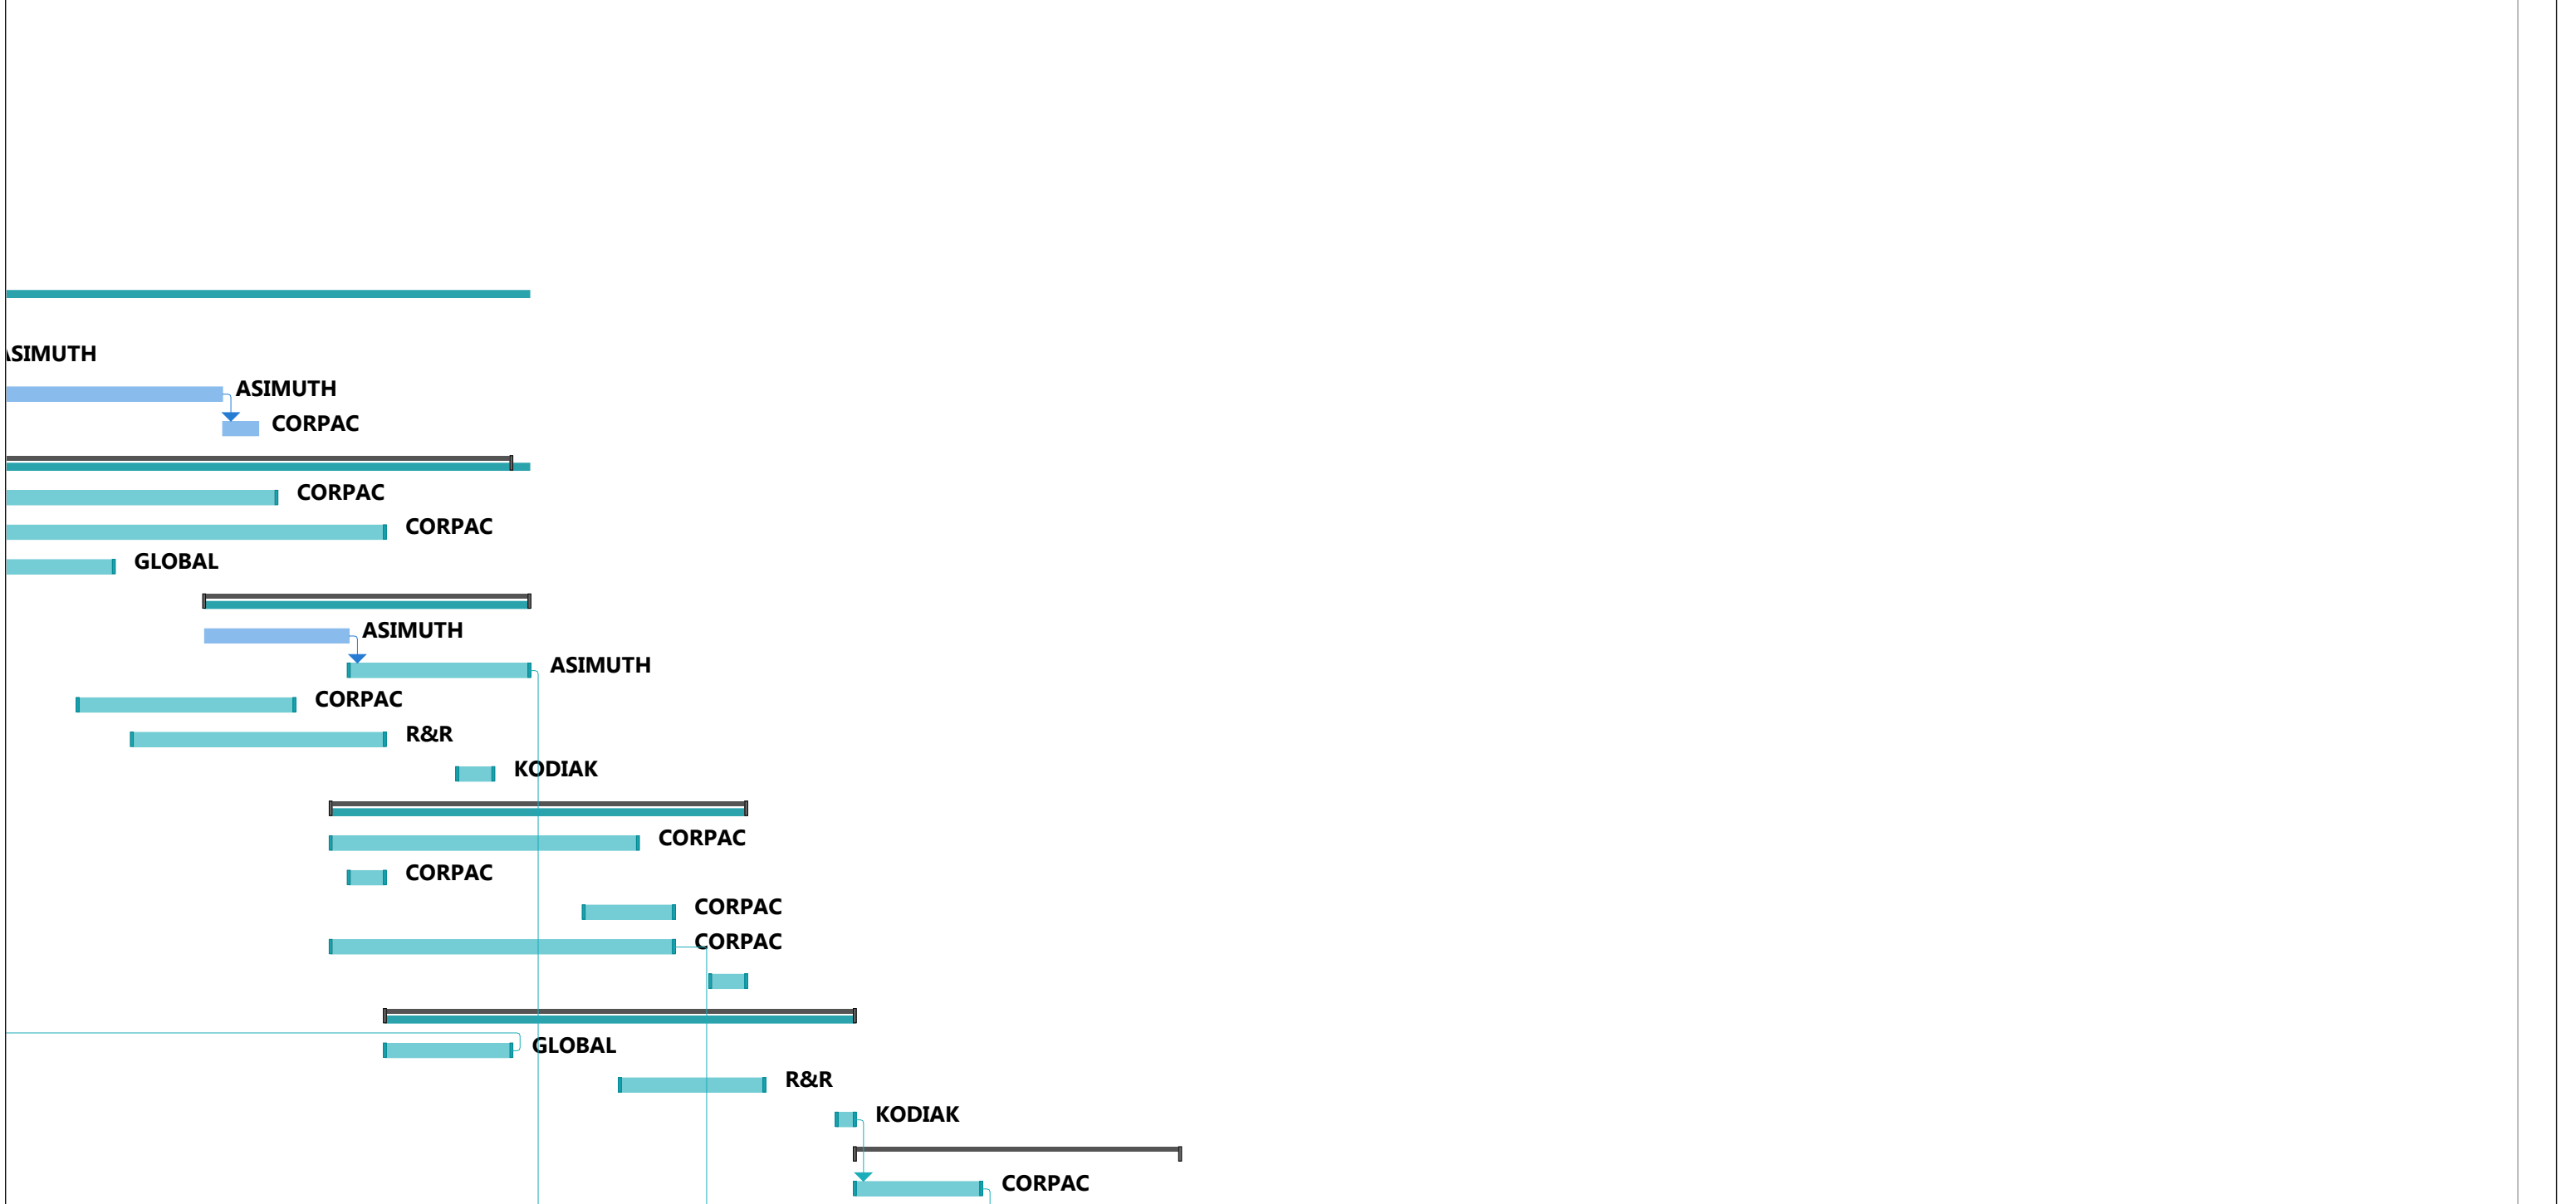


Project: 20TH AVE. LID
 Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

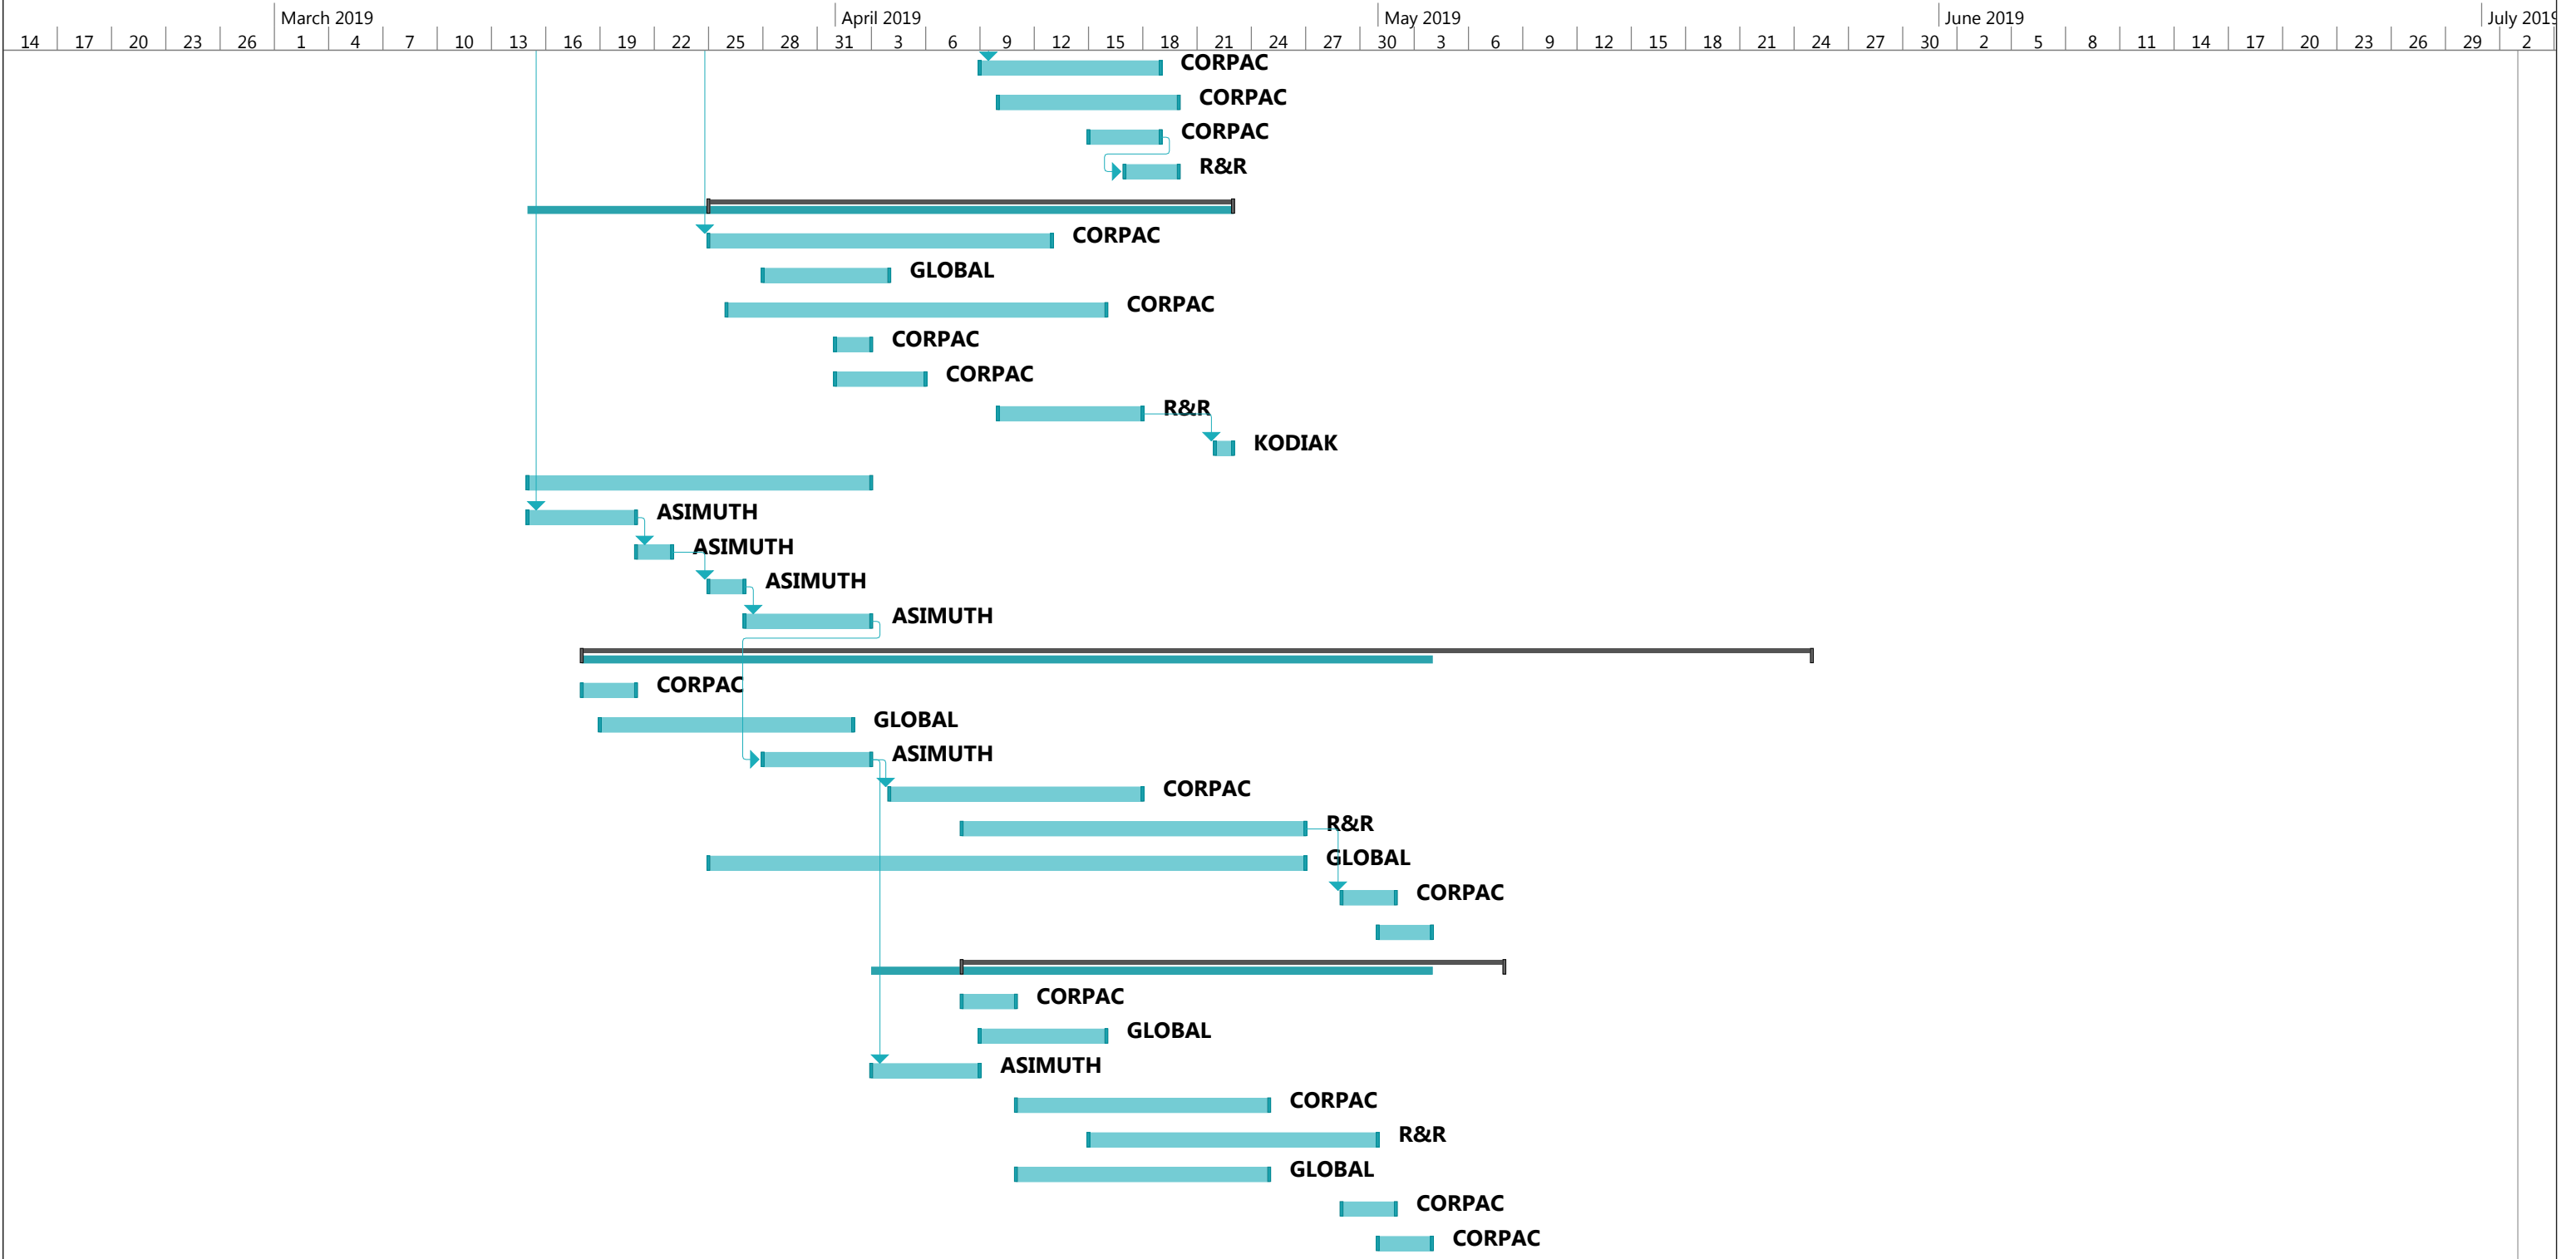

Project: 20TH AVE. LID
Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

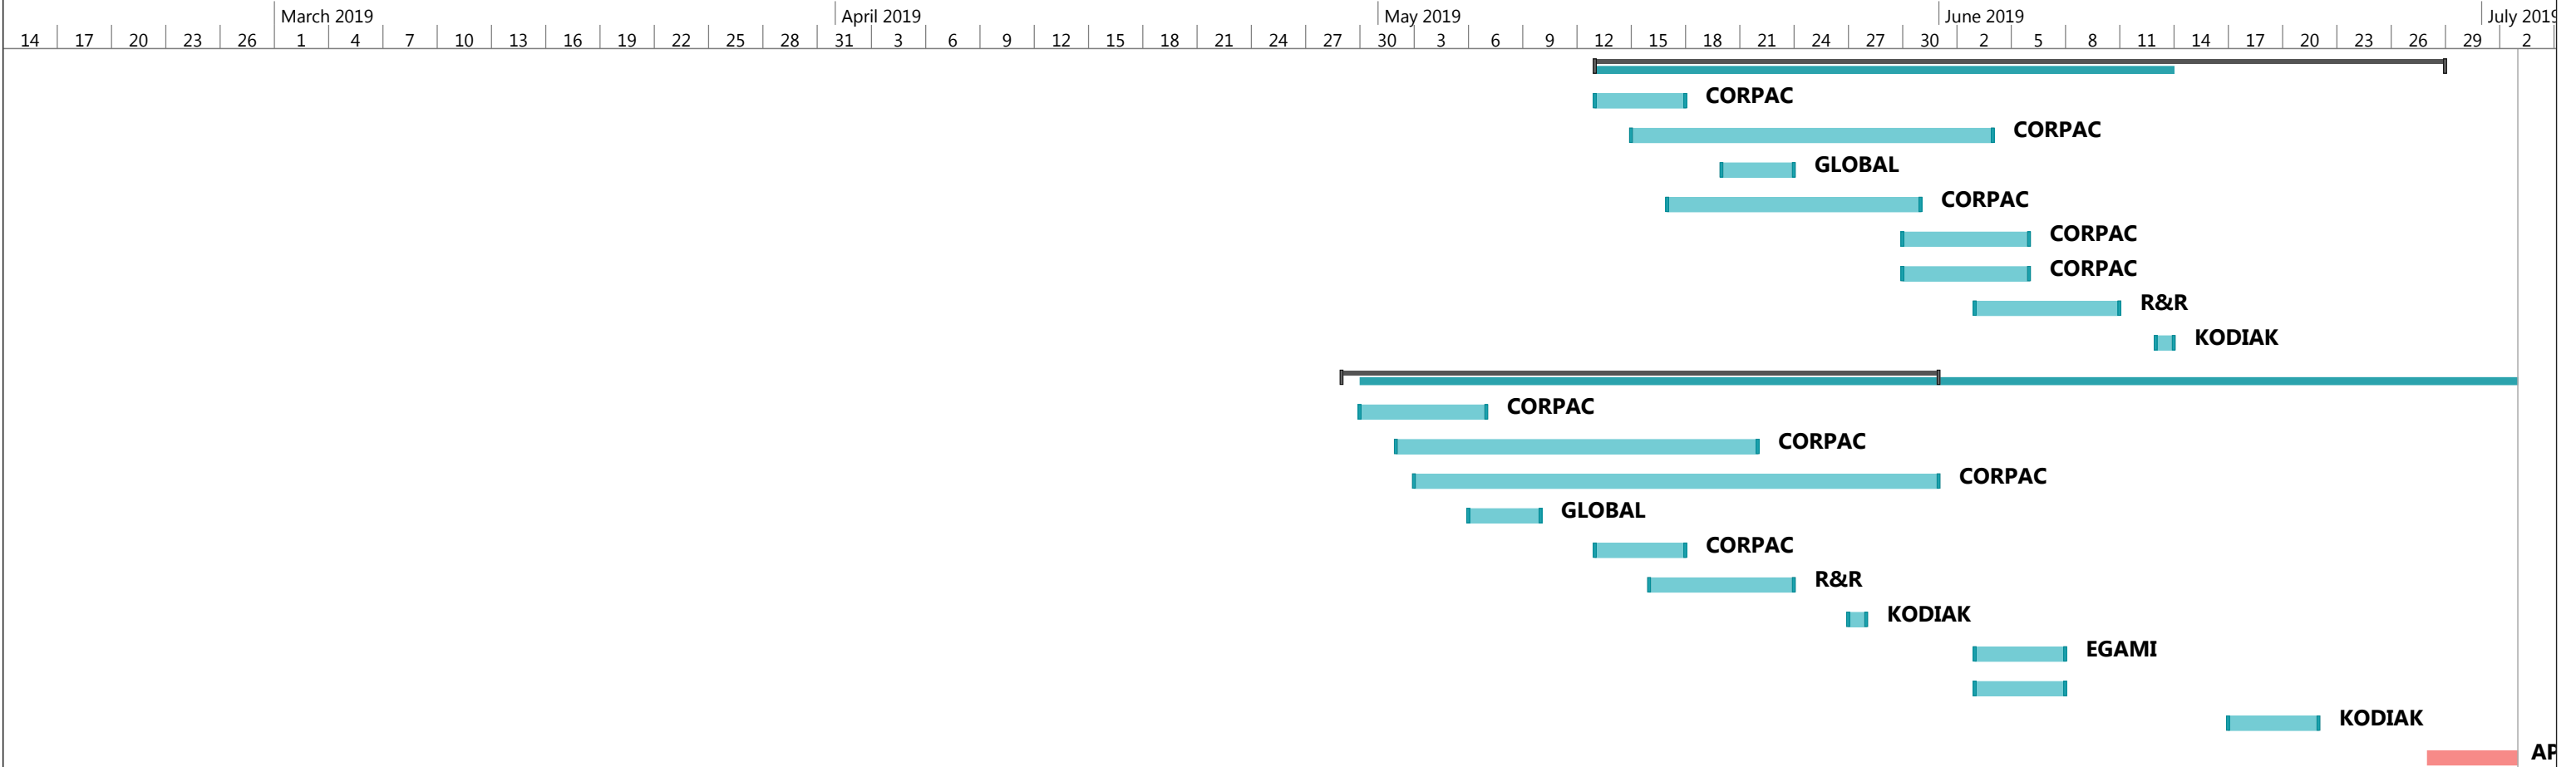

Project: 20TH AVE. LID
Date: 2/5/2019

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			
