



South Waterfront Greenway Construction Update November 11, 2013

Happy Veterans Day!


Construction

Phase 1 heavy construction is nearly complete. All that remains is installation of the safety railings at the top of the retaining walls, some planting and site clean up and then to install the final site fencing.

Fencing

As we have been emphasizing in our updates for the past year, the fencing will need to stay up until the lawns have grown in enough to withstand typical park foot traffic and maintenance activities. This is expected to be late next spring - approximately June of 2014 - based on normal growing conditions.

In the meantime, we received a request from the Nature and Greenspaces Committee to try to find a way to configure the fencing so that folks could get to the river access ramp. We are glad to say that a route through is available – see the diagram below:

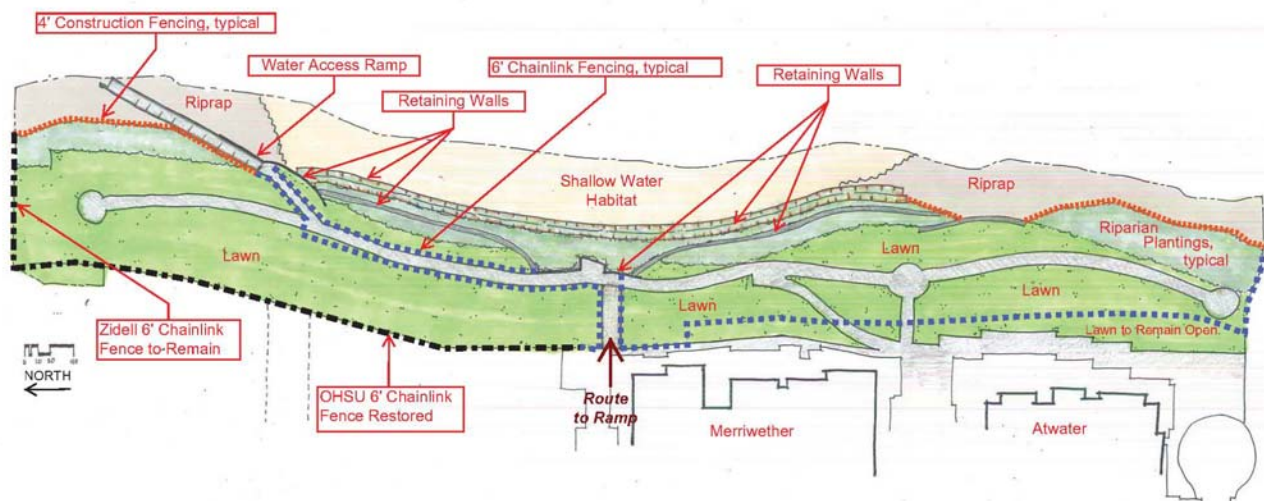

Fence Lines: After Construction, Until Lawns Established

South Waterfront Greenway - Central District
October 10, 2013

Work Hours: Monday – Friday, 7:00 a.m. to 7:00 p.m.

Contact Us

The Portland Parks & Recreation website at www.portlandparks.org is the place to go for accurate and up-to-date information on the progress of the project. We know that construction is inconvenient, messy and sometimes dangerous. By providing accurate and timely information, we will do our best to let you know what to expect.

Elizabeth Kennedy-Wong
502-823-5113

elizabeth.kennedy-wong@portlandoregon.gov
